

July 13, 2023

Project No. T05-BE

## NOTICE TO RESIDENTS / PROPERTY OWNERS

### Dayfoot Street Improvements – Phase 1 Dayfoot Street from Lilly Street to Danielle Gate

## Construction Update Notice

The **Dayfoot Street Sanitary Trunk Sewer – Phase 1** project started on February 7, 2023 by John Bravakis Enterprises Ltd. ("Contractor"). This Notice to Residents and Property Owners summarizes the works completed to date and the anticipated works to occur during the month of July.

### Completed Works

In June 2023, the Contractor:

- Installed an Oil Grit Separator (OGS) Unit on English Drive.
- Completed cut and cap on existing watermain in English Drive and Centre Street intersection.
- Removed existing sanitary manhole in English Drive and Centre Street intersection and connected existing sanitary main with new pipe.
- Filled existing sanitary main on English Drive with grout.
- Located existing sanitary services on Dayfoot Street.
- Removed and replaced existing culvert on the North side of Centre Street and English Drive intersection leading East/West.
- Installed watermain on English Drive along with services.
- Installed storm main on English Drive along with services including a riser pipe for overland flow and sump pump discharge to drain into.
- Installed catchbasins and double catchbasins on English Drive.
- Installed a sanitary bypass system on Dayfoot Street to ensure undisturbed flows.
- Started installing sanitary main on Dayfoot Street and connected to existing manhole at the North limit. Installed pipe from the North to South.
- Installed and connected sanitary services while installing sanitary main on Dayfoot Street.
- Installed gate valve on existing watermains at the West limit of McKeown Street and Thomas Street.
- Started installing watermain on Dayfoot Street leading South from English Drive.
- Started constructing road with granular material on English Drive. Installed underground utility ducts on English Drive.

## Scheduled Works

During July, the Contactor will:

- **Close Dayfoot Street from Lilly Street to Stewart Street and English Drive, from Centre Street to Dayfoot Street Monday, May 1, 2023** until completion, which is anticipated for **September 1, 2023.**
- Continue to install tree protection fencing and environmental control fencing within the project limits.
- Continue to remove existing signs and mailboxes that are in conflict with proposed construction activities.
- Continue installing sanitary sewer and services on Dayfoot Street.
- Continue installing watermain on Dayfoot Street.
- Start dewatering on Dayfoot Street, North of English Drive.


Please be advised that these scheduled works are weather dependant and subject to delays due to unforeseen circumstances.

Construction and advisory signs will be erected before construction begins. Signed detour routes will be provided to direct motorists around the road closure. We advise that when you drive or walk through or around the construction work zone, that you obey the construction signage for your safety and for the safety of the workers.

You will experience some delays and inconvenience during this time. In this regard, we respectfully ask for your cooperation and patience to complete this project in a timely manner. Should you have any questions or concerns related to this project, please contact the following project team:

<p><b>Field Construction Representative:</b></p> <p><b><u>Primary Contact for Inquiries</u></b></p> <p><u>Consultant Inspector</u></p> <p>Zach Mendes, B.Eng. C.F. Crozier &amp; Associates Inc. 51 John Street, P.O. Box 1011 Bradford, Ontario, L3Z 2B4 Office: 905-952-3111 Email: zmendes@cfcrozier.ca</p> <p><b><u>Secondary Contact for Inquiries</u></b></p> <p><u>Town Liaison</u></p> <p>Will Spence R.J. Burnside &amp; Associates Limited 128 Wellington Street West, Suite 301 Barrie, Ontario, L4N 8J6 Cell: 705-331-6314 Email: will.spence@rjburnside.com</p>	<p><b>Project Management Representatives:</b></p> <p><b><u>Other Project Contacts</u></b></p> <p><u>Consultant Construction Manager</u></p> <p>Shawn Landry C.F. Crozier &amp; Associates Inc. 51 John Street, P.O. Box 1011 Bradford, Ontario, L3Z 2B4 Office: 905-952-3111 Email: slandry@cfcrozier.ca</p> <p><u>Town Project Manager</u></p> <p>Rob Greenwood, PMP, C.E.T. Project Manager, Capital Engineering Town of New Tecumseth 10 Wellington Street East Alliston, Ontario, L9R 1A1 Office: 705-415-1930 Email: rgreenwood@newtecumseth.ca</p>
--	--

## Work Area for Month of July 2023

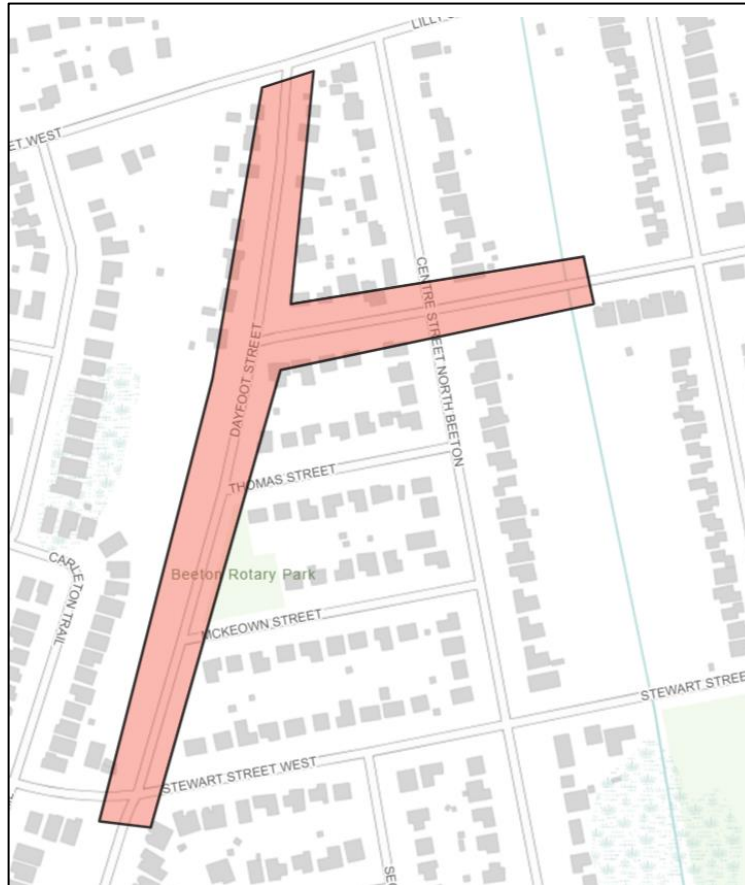

Project updates and notices will be provided on a regular basis to ensure residents and stakeholders stay informed of the progress of the works.

Electronic copies of all project updates and notifications can be found on the Town's website at [www.newtecumseth.ca/dayfoot](http://www.newtecumseth.ca/dayfoot) or by scanning the following QR code:



If you are the resident of the house and not the property owner, we request that you please forward this letter to the appropriate person/property owner.

### Project Updates

To stay up to date on project updates, please visit the Town's website at [www.newtecumseth.ca/dayfoot](http://www.newtecumseth.ca/dayfoot)
