

August 3, 2023

Project No. T05-BE

NOTICE TO RESIDENTS / PROPERTY OWNERS

Dayfoot Street Improvements – Phase 1 Dayfoot Street from Lilly Street to Danielle Gate

Construction Update Notice

The **Dayfoot Street Sanitary Trunk Sewer – Phase 1** project started on February 7, 2023 by John Bravakis Enterprises Ltd. ("Contractor"). This Notice to Residents and Property Owners summarizes the works completed in July and the anticipated works to occur during the month of August.

Completed Works

In July 2023, the Contractor:

- Installed sanitary main leading South on Dayfoot Street from Lilly Street to English Drive and continued installation leading South on Dayfoot Street from English Drive.
- Installed sanitary services and connected to existing (where applicable) following installation of sanitary main on Dayfoot Street between Lilly Street and English Drive.
- Installed sanitary bypass system on Dayfoot Street to ensure undisturbed flows.
- Filled existing sanitary main on Dayfoot Street, North of English Drive with grout.
- Installed watermain on Dayfoot Street from Lilly Street to Stewart Street.
- Installed hydrants on Dayfoot Street between Lilly Street and Stewart Street.
- Installed several water services on Dayfoot Street between Lilly Street and English Drive but did not connect to existing homes.
- Completed watermain cut and caps in Dayfoot Street and Stewart Street intersection.
- Removed dewatering system from Dayfoot Street.
- Stripped material and re-graded ditch on the North side of English Drive, East of Centre Street to ensure positive drainage towards storm drain.
- Removed existing street signs in conflict with proposed construction activities.

Scheduled Works

During August 2023, the Contactor will:

- Install curb and base asphalt on English Drive from Dayfoot Street to Centre Street and on Dayfoot Street from Lilly Street to English Drive with hopes of also completing Dayfoot Street from English Drive to Thomas Street.
- Continue to install tree protection fencing and environmental control fencing within the project limits as they progress further South on Dayfoot Street.
- Continue to remove existing signs and mailboxes that are in conflict with proposed construction activities as they progress further South on Dayfoot Street.

- Continue installing sanitary sewer and services on Dayfoot Street from Thomas Street to Stewart Street.
- Install storm main and services on Dayfoot Street from Lilly Street to Thomas Street.
- Potentially commission new watermain on Dayfoot Street and English Drive and remove temporary water supply system.


Please be advised that these scheduled works are weather dependant and subject to delays due to unforeseen circumstances.

Construction and advisory signs will be erected before construction begins. Signed detour routes will be provided to direct motorists around the road closure. We advise that when you drive or walk through or around the construction work zone, that you obey the construction signage for your safety and for the safety of the workers.

You will experience some delays and inconvenience during this time. In this regard, we respectfully ask for your cooperation and patience to complete this project in a timely manner. Should you have any questions or concerns related to this project, please contact the following project team:

<p>Field Construction Representative:</p> <p><u>Primary Contact for Inquiries</u></p> <p><u>Consultant Inspector</u></p> <p>Zach Mendes, B.Eng. C.F. Crozier & Associates Inc. 51 John Street, P.O. Box 1011 Bradford, Ontario, L3Z 2B4 Office: 905-952-3111 Email: zmendes@cfcrozier.ca</p> <p><u>Secondary Contact for Inquiries</u></p> <p><u>Town Liaison</u></p> <p>Will Spence R.J. Burnside & Associates Limited 128 Wellington Street West, Suite 301 Barrie, Ontario, L4N 8J6 Cell: 705-331-6314 Email: will.spence@rjburnside.com</p>	<p>Project Management Representatives:</p> <p><u>Other Project Contacts</u></p> <p><u>Consultant Construction Manager</u></p> <p>Shawn Landry C.F. Crozier & Associates Inc. 51 John Street, P.O. Box 1011 Bradford, Ontario, L3Z 2B4 Office: 905-952-3111 Email: slandry@cfcrozier.ca</p> <p><u>Town Project Manager</u></p> <p>Rob Greenwood, PMP, C.E.T. Project Manager, Capital Engineering Town of New Tecumseth 10 Wellington Street East Alliston, Ontario, L9R 1A1 Office: 705-415-1930 Email: rgreenwood@newtecumseth.ca</p>
--	--

Work Area for Month of August 2023

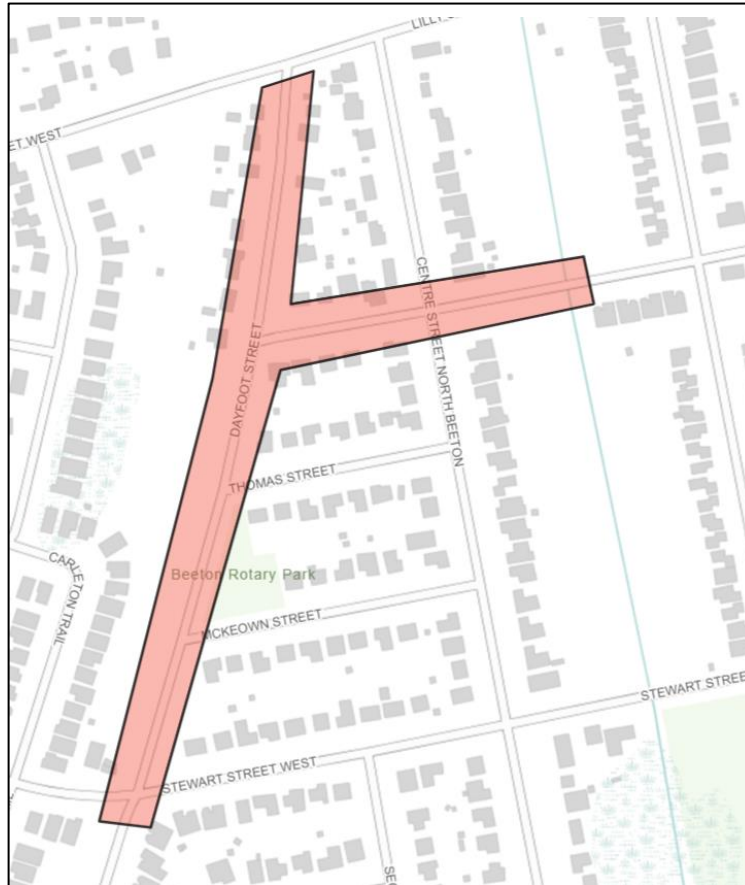

Project updates and notices will be provided on a regular basis to ensure residents and stakeholders stay informed of the progress of the works.

Electronic copies of all project updates and notifications can be found on the Town's website at www.newtecumseth.ca/dayfoot or by scanning the following QR code:



If you are the resident of the house and not the property owner, we request that you please forward this letter to the appropriate person/property owner.

Project Updates

To stay up to date on project updates, please visit the Town's website at www.newtecumseth.ca/dayfoot
