

September 7, 2023

Project No. T05-BE

NOTICE TO RESIDENTS / PROPERTY OWNERS

Dayfoot Street Improvements – Phase 1 Dayfoot Street from Lilly Street to Danielle Gate

Construction Update Notice

The **Dayfoot Street Sanitary Trunk Sewer – Phase 1** project started on February 7, 2023 by John Bravakis Enterprises Ltd. ("Contractor"). This Notice to Residents and Property Owners summarizes the works completed in August and the anticipated works to occur during the month of September.

Completed Works

In August 2023, the Contractor:

- Installed sanitary sewer and services on Dayfoot Street from Thomas Street to the North side of Stewart Street intersection.
- Installed storm sewer and services on Dayfoot Street from Lilly Street to the North side of Stewart Street intersection.
- Raised frame and grates on all catch basins and maintenance holes to base asphalt elevation.
- Installed granular material for road makeup and fine graded.
- Installed curb and base asphalt on English Drive between Dayfoot Street and Hendrie Drain and on Dayfoot Street from Lilly Street to the South side of McKeown Street intersection.
- Began stripping topsoil up to property line for homes located South of Stewart Street intersection.
- Continued to remove existing street signs that are in conflict with proposed construction activities.
- Painted temporary line painting on base asphalt.
- Installed stop signs at intersections.

Scheduled Works

During September 2023, the Contactor will:

- Install sanitary sewer and services leading South on Dayfoot Street through Stewart Street intersection and connect to existing on Stewart Street and Julia Drive.
- Install storm main and services leading South on Dayfoot Street through Stewart Street intersection and connect to existing on Stewart Street.
- Install watermain and services leading South on Dayfoot Street through Stewart Street intersection and connect to existing on Stewart Street and Julia Drive.
- Install underground utility ducts and duct crossings.

- Install curb and base asphalt on Dayfoot Street from the South side of McKeown Street to the South side of Stewart Street intersection.
- Install asphalt ramping along edge of curb previously poured on Dayfoot Street and English Drive.
- Commission new watermain and services for Phase 1 and remove temporary water supply system.
- Install and commission temporary water supply system for Phase 2.
- Install sidewalk on Dayfoot Street from Lilly Street to Stewart Street and on English Drive from Dayfoot Street to Hendrie Drain.


Please be advised that these scheduled works are weather dependant and subject to delays due to unforeseen circumstances.

Construction and advisory signs will be erected before construction begins. Signed detour routes will be provided to direct motorists around the road closure. We advise that when you drive or walk through or around the construction work zone, that you obey the construction signage for your safety and for the safety of the workers.

You will experience some delays and inconvenience during this time. In this regard, we respectfully ask for your cooperation and patience to complete this project in a timely manner. Should you have any questions or concerns related to this project, please contact the following project team:

<p>Field Construction Representative:</p> <p><u>Primary Contact for Inquiries</u></p> <p><u>Consultant Inspector</u></p> <p>Zach Mendes, B.Eng. C.F. Crozier & Associates Inc. 51 John Street, P.O. Box 1011 Bradford, Ontario, L3Z 2B4 Office: 905-952-3111 Email: zmendes@cfcrozier.ca</p> <p><u>Secondary Contact for Inquiries</u></p> <p><u>Town Liaison</u></p> <p>Will Spence R.J. Burnside & Associates Limited 128 Wellington Street West, Suite 301 Barrie, Ontario, L4N 8J6 Cell: 705-331-6314 Email: will.spence@rjburnside.com</p>	<p>Project Management Representatives:</p> <p><u>Other Project Contacts</u></p> <p><u>Consultant Construction Manager</u></p> <p>Shawn Landry C.F. Crozier & Associates Inc. 51 John Street, P.O. Box 1011 Bradford, Ontario, L3Z 2B4 Office: 905-952-3111 Email: slandry@cfcrozier.ca</p> <p><u>Town Project Manager</u></p> <p>Rob Greenwood, PMP, C.E.T. Project Manager, Capital Engineering Town of New Tecumseth 10 Wellington Street East Alliston, Ontario, L9R 1A1 Office: 705-415-1930 Email: rgreenwood@newtecumseth.ca</p>
--	--

Work Area for Month of September 2023

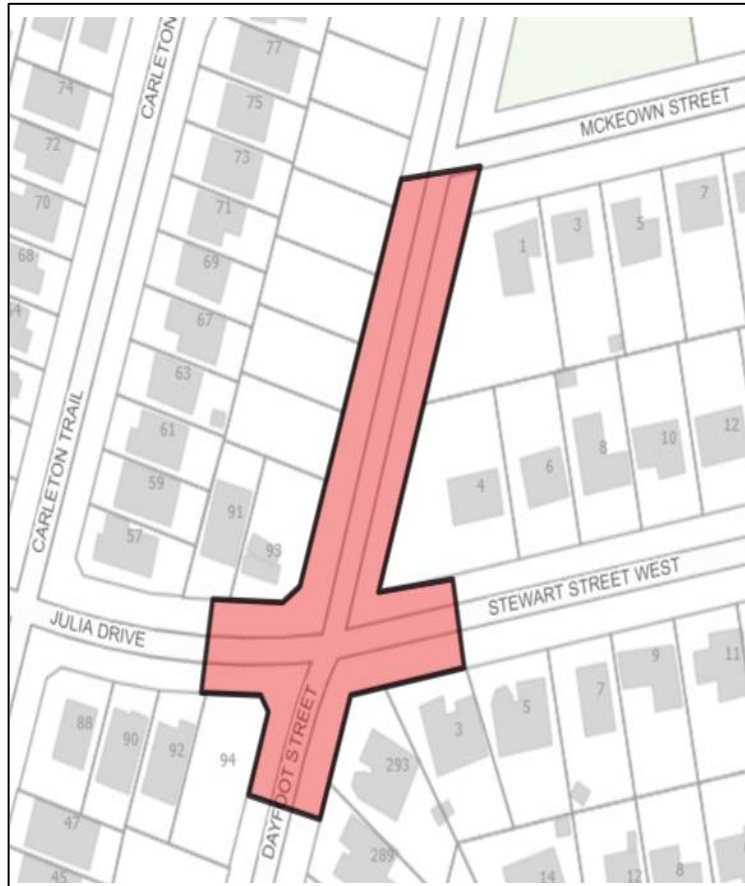

Project updates and notices will be provided on a regular basis to ensure residents and stakeholders stay informed of the progress of the works.

Electronic copies of all project updates and notifications can be found on the Town's website at www.newtecumseth.ca/dayfoot or by scanning the following QR code:



If you are the resident of the house and not the property owner, we request that you please forward this letter to the appropriate person/property owner.

Project Updates

To stay up to date on project updates, please visit the Town's website at www.newtecumseth.ca/dayfoot
